
Gateway Boulevard

- 1. This week of January 22-26, Brown Contracting and boring subcontractor completed the installation of four water service mains and one 8" water main across gateway Boulevard. City crews will complete the chlorination and pressure testing of the 8" main on Monday, January 29.
- 2. During the week of January 29-February 2 Brown Contracting is scheduled to complete the following, weather permitting:
 - Backfill 8" trench
 - Complete AC Patching trench across roadway & storm trench.
 - Complete sidewalk patching at water connections.
 - Begin excavation for south sidewalk ramps.
 - Set & place south ADA ramp.
 - Excavate for north ADA ramp & sidewalk.
- 3. During the weeks of February 5 February 16, 2018, Brown will complete the following, weather permitting:
 - a. Close driveway for new construction (February 6)
 - b. Complete construction of ADA ramps
 - c. Excavate and rock new concrete roadway
 - d. Set up valley gutter, place & finish driveway paving
 - e. Saw cut new construction joints
 - f. Allow driveway to cure.
- 4. February 16, weather permitting, is the deadline to complete the Gateway project.

Where possible, pedestrian access will be maintained using steel plates over sidewalk sections that have been removed.

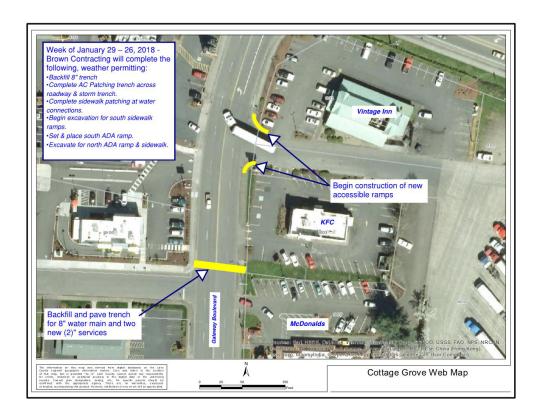


Row River Road Pedestrian Crossing

This pedestrian crossing is located on Row River Road between Chevron and Arby's and will provide a pedestrian refuge in the center turn lane and include flashing beacons to alert drivers.

The contractor, Pacific Excavation, is on schedule.

- 1. During the weeks of January 29 through March 2, 2018, Pacific Excavation is scheduled to complete the following, weather permitting:
 - a. Pour concrete for lighted pole foundations, sidewalks and accessible ramps, and the concrete median.
- 2. During the weeks of February 25, 2018, the contractor will install the poles and complete all electrical wiring.

Pedestrian access is currently maintained through the site using construction fencing with a compacted gravel surface.

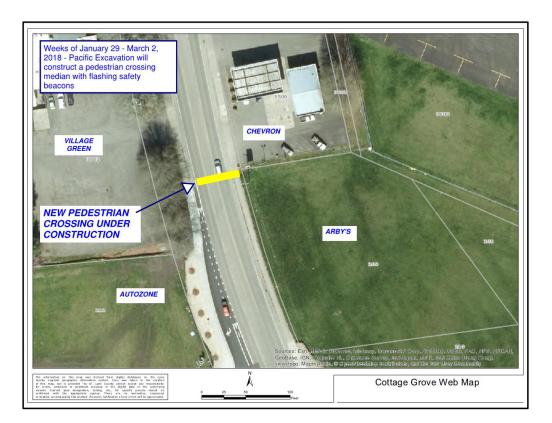

Project:	5332 - N. Gateway Improvements	SI										atus:	s: Open					I	Date	: 1	/29/2	018	Schedule No.: 1						
Act ID	Description	Prior Week						Week 1						Week 2							Week 3								
		22				26							2	3		5								13				17	18
		Μ	Т	W	Т	F	S	S	М	Т	W	Т	F	S	S	М	Т	W	Т	F	S	S	М	Т	W	Т	F	S	S
																							_						
	Lay 8" water line w/ 2" HDPE																						_						
	Testing of 8" water line																												
	Boring of 2" water, 4:00 am start																												
	Make connections to existing																												
	Backfill 8" trench with CLSM																												
	AC Patching trench across roadway & storm trench																												
	Sidewalk patch backs at water connections																												
	Driveway for reconstruction																												
	Excavate for south sidewalk ramps																												
	Set up & place south ADA ramp																												
	Excavate for north ADA ramp & sidewalk																												
	Set up & place north ADA ramp																												
	Close Driveway																												
	Excavate and rock new concrete roadway																												
	Set up valley gutter																												
	Place & finish valley gutter																												
	Set up for driveway paving																												
	Place & finish driveway paving																												
	Saw cut joints																												
	Concrete Cure Time																												
																						-							
																						-							
																											-		
																				-							-		
																				-							-		
																				-							-		
																				-									
																				-									
																				-									
