

## City work within the Right-of-Way


In the coming week, the City crews will complete the following work within the public right-of-way:

1. Tuesday, March 13 - Repair a leak on the water service at 1054 Van Buren.
2. Wednesday, March 14 - Replace a 2" gate valve in the cul-de-sac of East Jackson Avenue.

## Gateway Boulevard

Gateway Boulevard and the main driveway were opened last week for normal vehicle traffic with the completion of paving the transition panels.


The last phase of the project will occur in late March or early April, and will include cold-planing the existing pavement and applying new asphalt, striping and vehicle detector loops. This work will be located within Gateway Boulevard, extending south approximately 210-feet from the CG Connector intersection. The work will occur when temperatures are sufficiently high enough to meet ODOT specifications for paving the top course of asphalt.

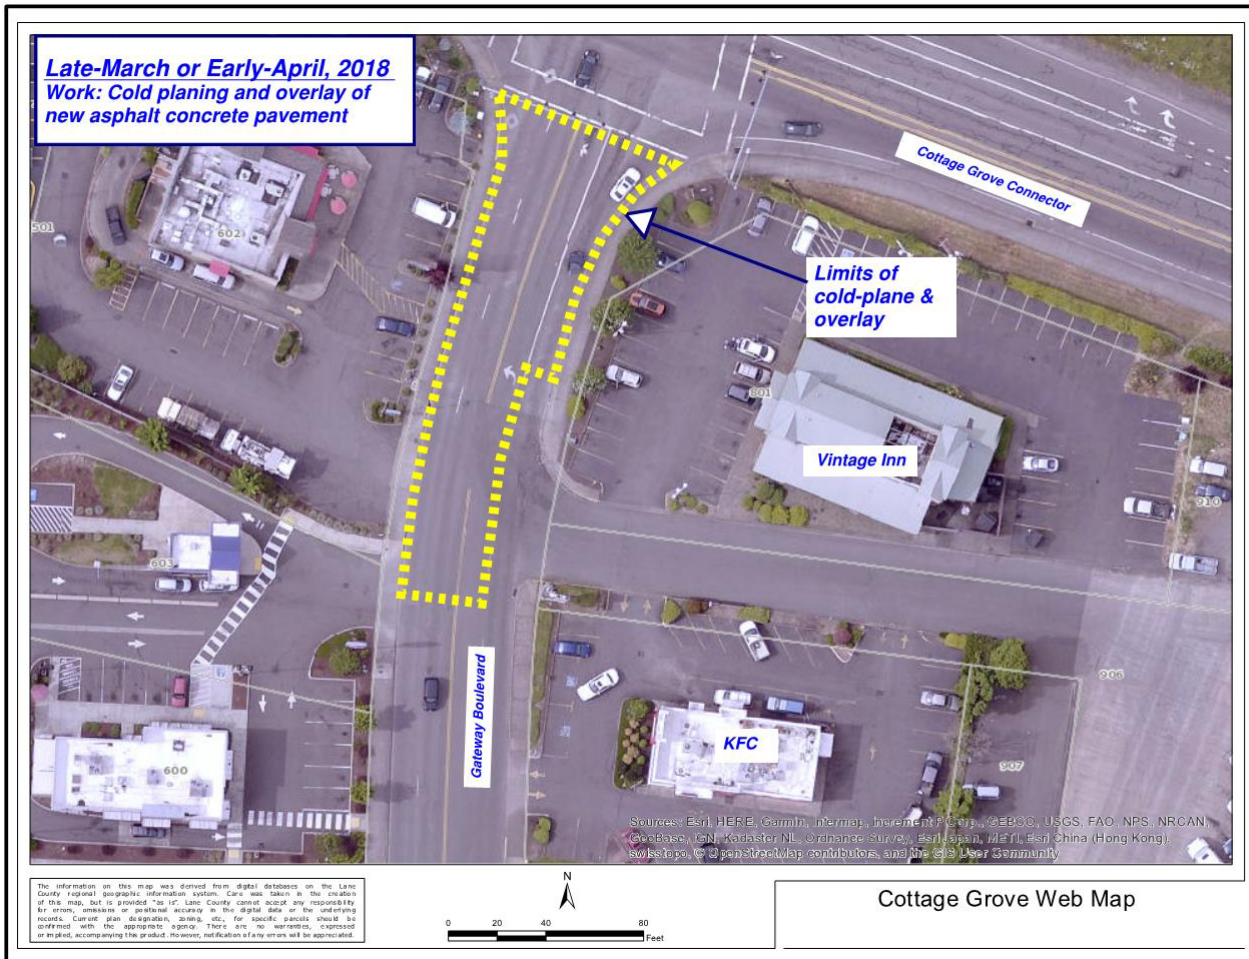

## Highway 99

On Wednesday, February 21, city crews completed a repair to the existing 12" sanitary sewer pipe located under the southbound lanes at Highway 99 and E Adams. This work resulted in saw cutting and removing a portion of the state's concrete roadway surface.

A contractor will return to the site to replace the temporary cold patch with reinforced, 8"-thick new concrete pavement, pending the City's approval of costs and timeline, as well as issuance of a work permit by Oregon Department of Transportation.

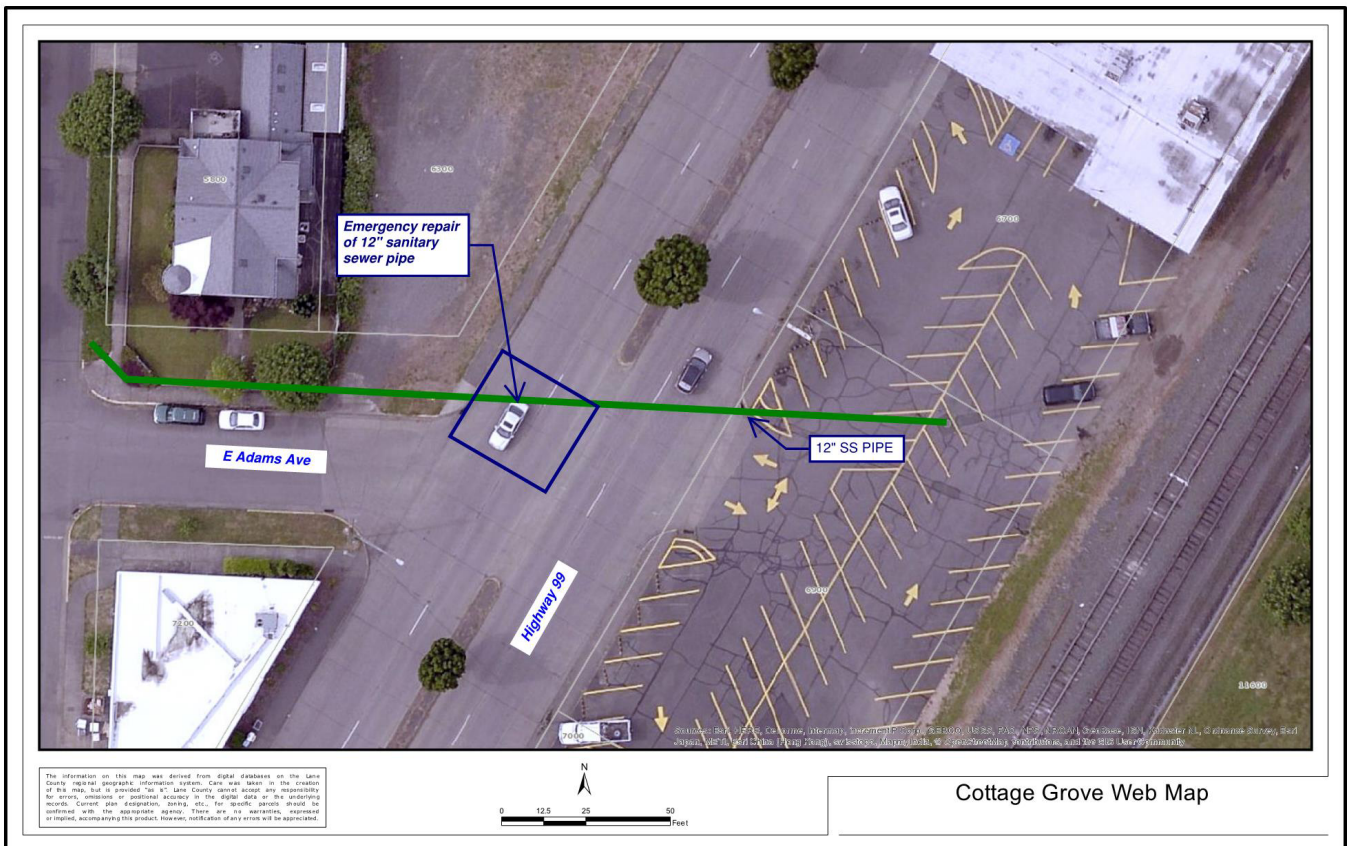

## Row River Road Pedestrian Crossing

To date, Pacific Excavation has completed the construction of sidewalks, ramps, a pedestrian refuge island and almost all striping.

- Flashing beacon pedestals were installed on Thursday, March 8, along with new electrical wiring and signage.
- The beacons will become operational once the software and programming are installed within two to three weeks.

At that time, City engineering staff will review all work as part of project-closeout procedures to confirm Final Completion.

