
City work within the Right-of-Way

In the coming week, the City crews will complete the following work within the public right-of-way:

1. Tuesday, March 20 – the crew will be working within the southbound lanes of *Highway 99 at E Adams Avenue* to remove old concrete and temporary pavement; Brown Contracting will then construct 8" of new concrete slab.

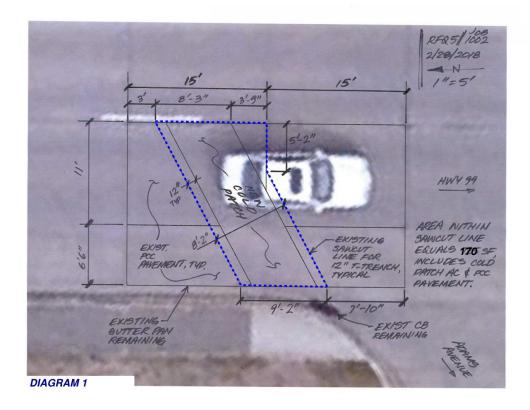

2. Friday, March 23 – the crew will be removing concrete sidewalk and a tree stump located adjacent to *35 S 6th Street*. On Monday, March 26, a contractor will pour a new 8'x16' sidewalk.

Row River Road Pedestrian Crossing

- Beacons were programmed and are now operational.
- The project will be considered complete pending inspections by Oregon Department of Transportation and City engineering staff, which are tentatively scheduled to occur within the next two weeks.



Row River Road – New Pedestrian Crossing

Gateway Boulevard

Gateway Boulevard and the main driveway were opened last week for normal vehicle traffic with the completion of paving the transition panels.

The last phase of the project will occur in late March or early April, and will include cold-planing the existing pavement and applying new asphalt, striping and vehicle detector loops. This work will be located within Gateway Boulevard, extending south approximately 210-feet from the CG Connector intersection. The work will occur when temperatures are sufficiently high enough to meet ODOT specifications for paving the top course of asphalt.

